

ANSER  
ADVISORY

SMMA



CONSIGLI  
Est. 1903




# City of Lawrence Henry K. Oliver School

## LAE Board Meeting

### Project Update


November 8, 2023

# Schedule

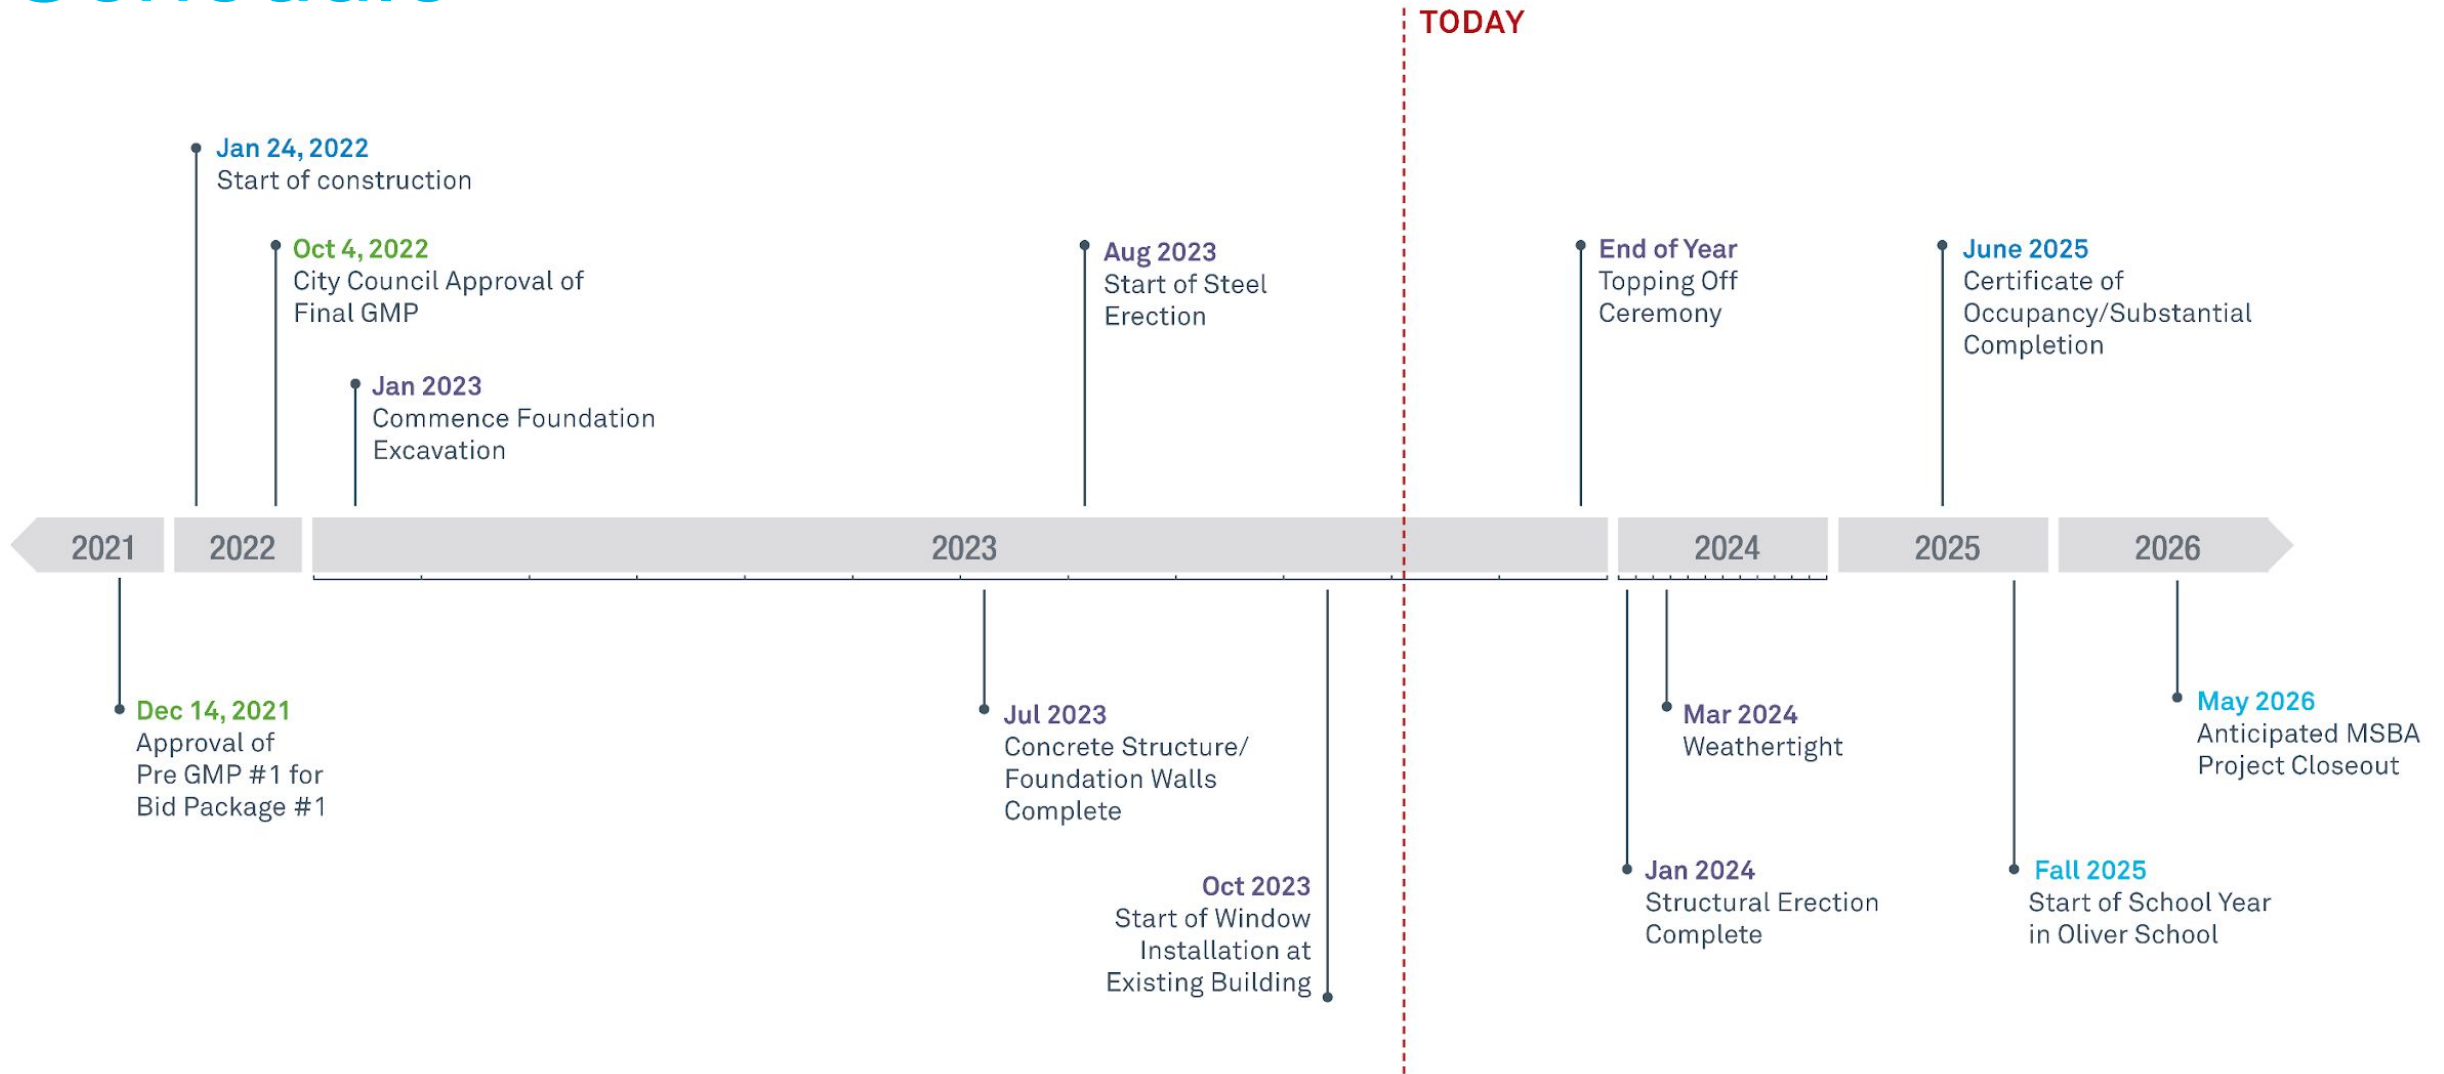

# FF&E Procurement

- Mar-May 2024: Furniture & Equipment Programming with User Groups
- Jun-Jul 2024: Documentation
- Aug-Oct 2024: Bidding/Purchase from State Contracts
- Oct 2024 – Jun 2025: Manufacture
- July 2025: Installation

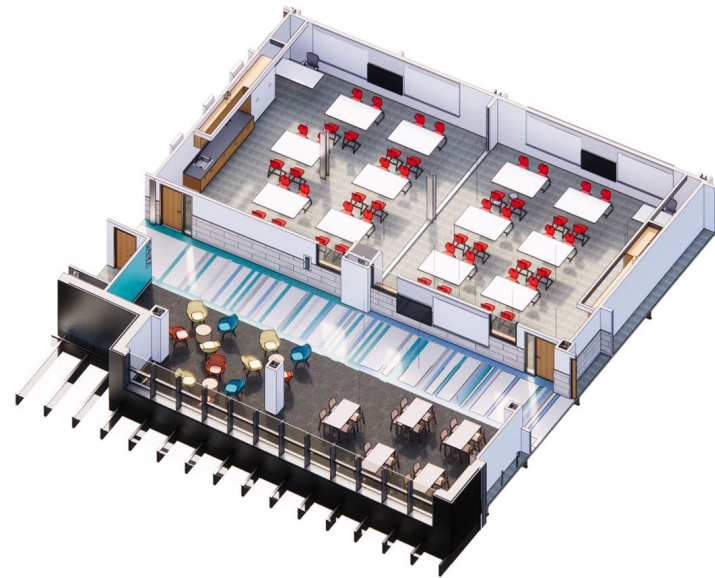


# Project Status

- July 2023: Concrete Structure/Foundation Complete
- August 2023: Steel Erection Commenced
- November 29, 2023: Topping Off Ceremony
- January 2024: Structural Steel Complete
- Spring 2024: Begin FF&E Procurement Process
- June 2025: Substantial Completion



# Henry K. Oliver School November Photos

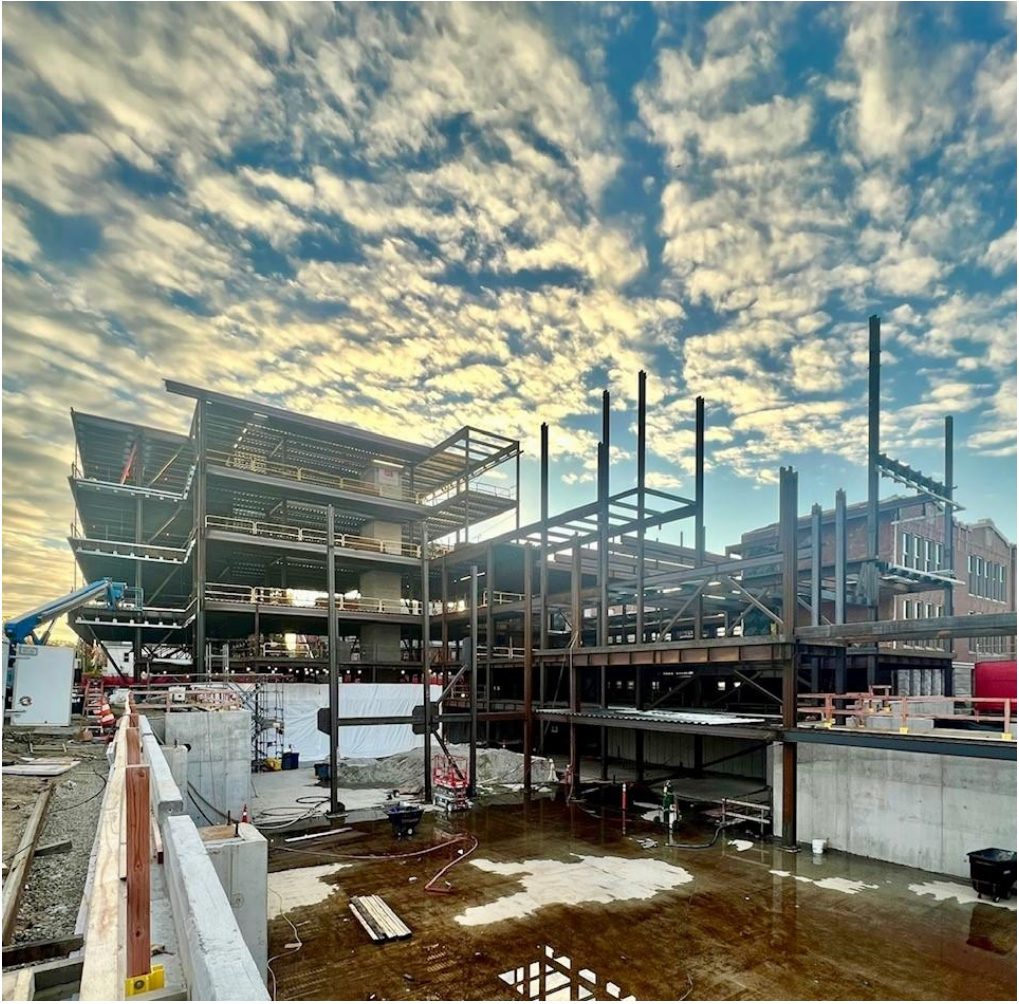

Steel Erection Complete – East Half



Steel Erection – Level 1 thru Roof



# Henry K. Oliver School November Photos



Stairwell



Replacement Windows – Existing Building



# Henry K. Oliver School Progress Photos



February 2022



October 2023



# Lawrence Oliver Monthly Update – November 2023

Link to Monthly  
Drone Video  
Footage:

<https://vimeo.com/877227310/1b66a89607?share=copy>

## Construction Updates

### Upcoming Activities

- Structural steel erection east – Levels 1-6
- Rebar install and concrete slab placements – west
- Existing building window install
- Electrical utility excavation

### Community Impacts

- Daily steel and decking deliveries through December
- Periodic concrete trucks for slab placements
- Periodic deliveries for misc. materials



Steel Erection – East Side



Stairwell



Drone Link:

<https://vimeo.com/877227310/1b66a89607?share=copy>



Steel Erection – East Side





# Thank you!

