


LEAHY SCHOOL PROJECT UPDATE

March 4, 2024

Progress through: February 29, 2024

- Structural steel erection was ongoing through the month and is currently approximately 80% complete. During the month there were 4 days with precipitation/wind that impacted structural steel progress.
- Under-slab plumbing and electric work began in the NW half of the building, working across, during the 3rd week and remains ongoing.
- The masons mobilized and began setting scaffolding at Stair# 2 and 4. CMU installation is scheduled to begin during the first week of March.
- Safety: Fire watch protocol is in place.
- Traffic interruptions are expected to continue at Erving Ave. and Bruce St. for deliveries during the daytime hours.

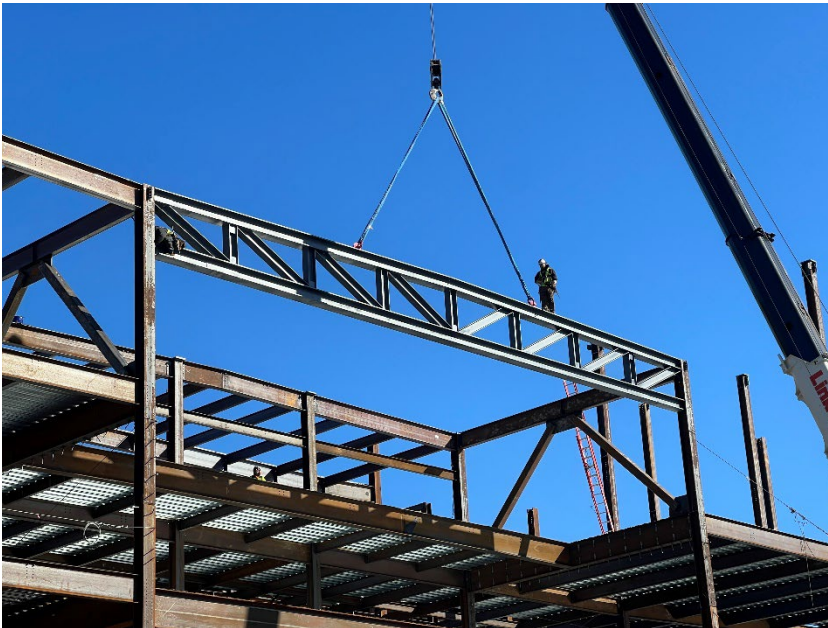

The first roof truss being installed over the roof on February 8, 2024.



Aerial view taken on February 12, 2024.



Phase 3 of 3 steel erection commenced on February 16, 2024 and continues.



Progress of Phase 3 steel work as of February 29, 2024.



Underground plumbing and electrical work began on February 13, 2024, and continues.



Electrical underground conduit installation, as of February 20, 2024, and ongoing currently.



The elevator oil separator tank piping progress as of February 29, 2024.
