


ID	Task Mode	Task Name	Duration	Start	Finish	Predecessor	2020	2021	2022	2023	2024	2025
							H1	H2	H1	H2	H1	H2
1		Leahy Elementary School										
2		Procure OPM	56 days	Mon 6/3/19	Mon 8/19/19							
8		Procure Designer	169 days	Thu 6/6/19	Tue 1/28/20							
26												
27		Feasibility Study/Schematic Design	387 days	Mon 1/13/20	Tue 7/6/21							
28		LESBC meeting with Designer for Kick-off	1 day	Mon 1/13/20	Mon 1/13/20							
29		Visioning meeting	8 days	Tue 1/14/20	Thu 1/23/20	28						
30		Kick off meeting with LPS, MSBA, OPM	1 day	Wed 1/22/20	Wed 1/22/20							
31		Visioning meeting	7 days	Fri 1/24/20	Mon 2/3/20	29						
32		Visioning meeting	5 days	Tue 2/4/20	Mon 2/10/20	31						
33		Visioning meeting	10 days	Tue 2/11/20	Mon 2/24/20	32						
34		Community Input	0 days	Thu 2/27/20	Thu 2/27/20	33FS+3 da						
35		Community Input	0 days	Thu 2/27/20	Thu 2/27/20	33FS+3 da						
36		Preliminary Program	15 days	Thu 1/23/20	Wed 2/12/20	30						
37		Site Investigative with MVG Consultants	1 day	Thu 2/20/20	Thu 2/20/20							
38		LESBC Meeting - Report on Programming and Site Options	1 day	Mon 3/2/20	Mon 3/2/20							
39		Site Investigative with MVG Consultants	1 day	Wed 3/4/20	Wed 3/4/20	37FS+6 da						
40		Covid-19 closures	60 days	Fri 3/13/20	Thu 6/4/20							
41		Development of Alternatives	24 days	Tue 3/3/20	Fri 4/3/20	38						
42		Community Input-Cancelled due to Covid-19	0 days	Fri 4/3/20	Fri 4/3/20	41						
43		LESBC Meeting - Update Programming and Alternatives	1 day	Tue 4/28/20	Tue 4/28/20							
44		Review PDP/Educational Plan Schedule	5 days	Wed 4/29/20	Tue 5/5/20	43						
45		LESBC Meeting	1 day	Tue 5/5/20	Tue 5/5/20							
46		Review PDP/Educational Plan Schedule	5 days	Wed 5/6/20	Tue 5/12/20	45						

2020-11-30 LES Schedule Update


Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessor	2020		2021		2022		2023		2024		2025
							H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1
47	✓	Review PDP/Educational Plan Schedule	5 days	Wed 5/13/20	Tue 5/19/20	46											
48	✓	Review PDP/Educational Plan Schedule	5 days	Wed 5/20/20	Tue 5/26/20	47											
49	✓	Review PDP/Educational Plan Schedule	5 days	Wed 5/27/20	Tue 6/2/20	48											
50	✓	Review PDP/Educational Plan Schedule	5 days	Wed 6/3/20	Tue 6/9/20	49											
51	✓	LESBC Meeting - Approval of PDP Alternatives	0 days	Thu 6/11/20	Thu 6/11/20												
52	✓	Review PDP/Educational Plan Schedule	11 days	Thu 6/11/20	Thu 6/25/20	51											
53	✓	LESBC Meeting - Approval of Ed Plan and PDP submission	0 days	Thu 6/25/20	Thu 6/25/20	52											
54	✓	Finalize PDP/Educational Plan for Submission	7 days	Fri 6/26/20	Mon 7/6/20	53											
55	✓	LESBC Meeting - Approval of PDP submission	1 day	Tue 7/7/20	Tue 7/7/20	54											
56	✓	PDP Submission (on or before 7-8-20)	1 day	Wed 7/8/20	Wed 7/8/20	55											
57	✓	MSBA Staff PDP Review	23 days	Thu 7/9/20	Mon 8/10/20	56											
58	✓	LESBC Meeting - PSR update	1 day	Tue 8/4/20	Tue 8/4/20												
59	✓	LESBC Meeting - PDP Comments update	1 day	Tue 8/18/20	Tue 8/18/20												
60	✓	Address MSBA Staff PDP Comments	10 days	Tue 8/11/20	Mon 8/24/20	57											
61		Prepare Preliminary Preferred Schematic (PSR) Report	46 days	Tue 8/25/20	Tue 10/27/20	60											
62	✓	LESBC Meeting - PSR update	1 day	Tue 9/1/20	Tue 9/1/20												
63	✓	LESBC Meeting - PSR update	1 day	Tue 9/29/20	Tue 9/29/20												
64	✓	LAE Board Meeting - PSR update	1 day	Wed 10/7/20	Wed 10/7/20												
65	✓	LESBC Meeting PSR review	0 days	Tue 10/13/20	Tue 10/13/20	61											
66	✓	Finalize and Submit PSR to MSBA (on or before 10/27/20)	11 days	Tue 10/13/20	Tue 10/27/20	65											
67	✓	FAS Meeting	1 day	Wed 11/18/20	Wed 11/18/20												
68	✓	MSBA Staff PSR Review	16 days	Wed 10/28/20	Wed 11/18/20	66											
69		LESBC Meeting	1 day	Wed 12/2/20	Wed 12/2/20												

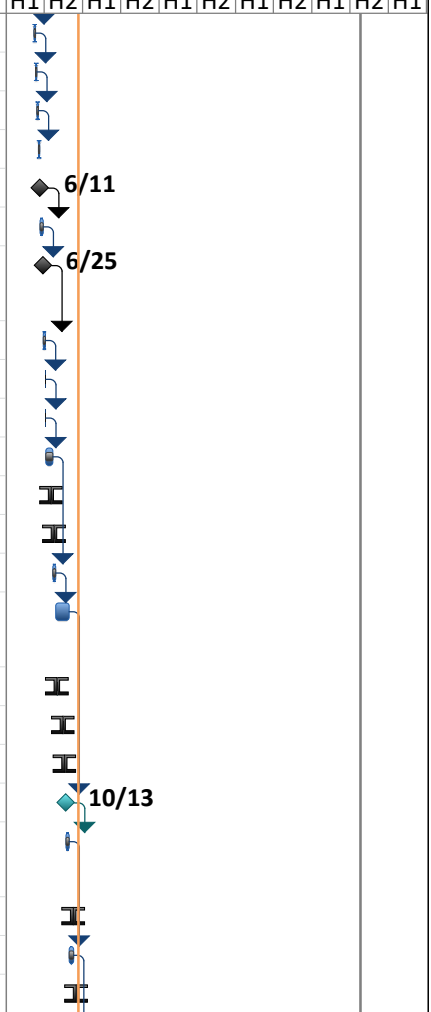

2020-11-30 LES Schedule Update	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	


ID	Task Mode	Task Name	Duration	Start	Finish	Predecessor	2020	2021	2022	2023	2024	2025
							H1	H2	H1	H2	H1	H2
70		Address MSBA Staff PSR Comments	15 days	Thu 11/19/20	Wed 12/9/20	68						
71		LESBC Meeting	1 day	Tue 12/22/20	Tue 12/22/20							
72		PSR MSBA Board Approval Target Date	1 day	Wed 12/16/20	Wed 12/16/20							
73		Develop Schematic Design (SD)	49 days	Thu 12/17/20	Tue 2/23/21	72						
74		LESBC Meeting	1 day	Tue 1/5/21	Tue 1/5/21							
75		Community Workshop I- SD	1 day	Tue 1/12/21	Tue 1/12/21							
76		LESBC Meeting	1 day	Tue 2/2/21	Tue 2/2/21							
77		Community Workshop -II SD	1 day	Tue 2/9/21	Tue 2/9/21							
78		LAE Board Meeting - SD update	1 day	Wed 2/24/21	Wed 2/24/21	73						
79		Submit SD to MSBA	1 day	Thu 2/25/21	Thu 2/25/21	78						
80		LESBC Meeting	1 day	Tue 3/2/21	Tue 3/2/21							
81		LESBC Meeting	1 day	Tue 4/6/21	Tue 4/6/21							
82		MSBA Staff Review	10 days	Fri 2/26/21	Thu 3/11/21	79						
83		Address MSBA Staff coments	10 days	Fri 3/12/21	Thu 3/25/21	82						
84		Project Scope & Budget MSBA Board Vote Target date	0 days	Wed 4/14/21	Wed 4/14/21							
85		Local Funding Authorization	60 days	Wed 4/14/21	Tue 7/6/21	84						
86		Design Development/Bidding/Construction	310 days	Tue 5/4/21	Mon 7/11/22							
87		Design Development (9 months)	180 days	Wed 7/7/21	Tue 3/15/22	85						
88		LESBC Meeting	1 day	Tue 5/4/21	Tue 5/4/21							
89		LESBC Meeting	1 day	Tue 6/8/21	Tue 6/8/21							
90		LESBC Meeting	1 day	Tue 7/13/21	Tue 7/13/21							
91		LESBC Meeting	1 day	Tue 8/3/21	Tue 8/3/21							
92		LESBC Meeting	1 day	Tue 8/31/21	Tue 8/31/21							
93		LESBC Meeting	1 day	Tue 10/5/21	Tue 10/5/21							
94		LESBC Meeting	1 day	Tue 11/2/21	Tue 11/2/21							

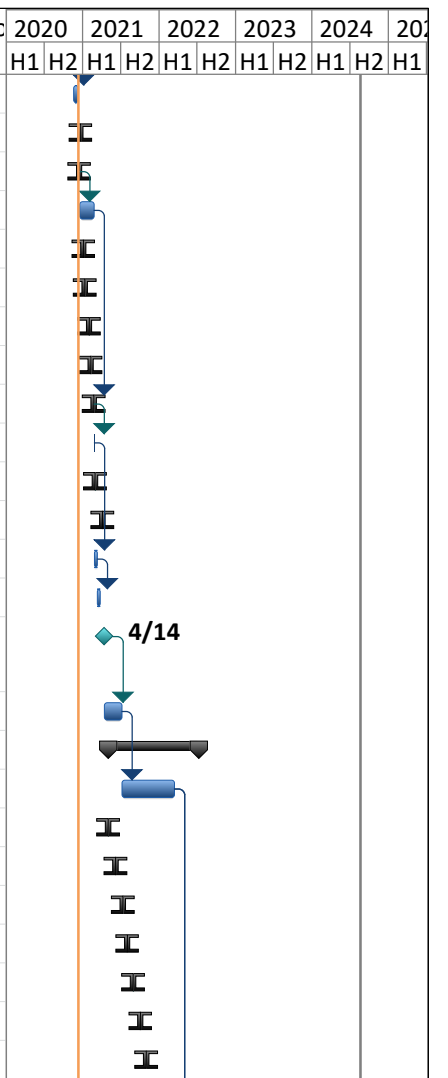

2020-11-30 LES Schedule Update

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessor	2020	2021	2022	2023	2024	2025
							H1	H2	H1	H2	H1	H2
95		Bid Abatement, Demo, and Utilities Packages	30 days	Wed 10/20/21	Tue 11/30/21	87FF-75 d						
96		Award Abatement, Demo, and Utilities Packages	20 days	Wed 12/1/21	Tue 12/28/21	95						
97		Move LESBC to Swing Space	7 days	Thu 12/23/21	Fri 12/31/21							
98		Abatement, Demo, and Utilities	100 days	Mon 1/3/22	Fri 5/20/22	96,97						
99		LESBC Meeting	1 day	Tue 12/7/21	Tue 12/7/21							
100		LESBC Meeting	1 day	Tue 1/4/22	Tue 1/4/22							
101		LESBC Meeting	1 day	Tue 2/1/22	Tue 2/1/22							
102		LESBC Meeting	1 day	Tue 3/1/22	Tue 3/1/22							
103		LESBC Meeting	1 day	Tue 4/5/22	Tue 4/5/22							
104		LESBC Meeting	1 day	Tue 5/3/22	Tue 5/3/22							
105		LESBC Meeting	1 day	Tue 6/7/22	Tue 6/7/22							
106		Bidding	50 days	Wed 3/16/22	Tue 5/24/22	87						
107		LESBC Meeting to review Bids and recommend Award	5 days	Wed 5/25/22	Tue 5/31/22	106						
108		Award Construction Contract	10 days	Wed 6/1/22	Tue 6/14/22	107						
109		LESBC Meeting	1 day	Mon 7/11/22	Mon 7/11/22							
110		Construction (26 months)	570 days?	Wed 6/15/22	Tue 8/20/24							
111		Construction (24 months)	480 days	Wed 6/15/22	Tue 4/16/24	108,98						
112		Commissioning and Punch List (2 Months)	30 days	Wed 4/17/24	Tue 5/28/24	111						
113		Move-in	60 days	Wed 5/29/24	Tue 8/20/24	112						
114												

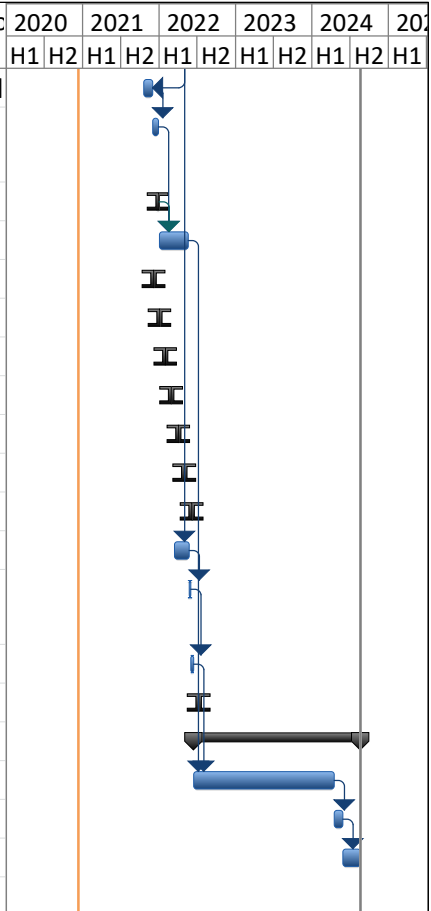

2020-11-30 LES Schedule Update

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	
