

ANSER
ADVISORY

SMMA



CONSIGLI
Est. 1903




City of Lawrence Oliver K-8 Educational Complex


LAE Board Meeting

Project Update

November 09, 2022



Schedule

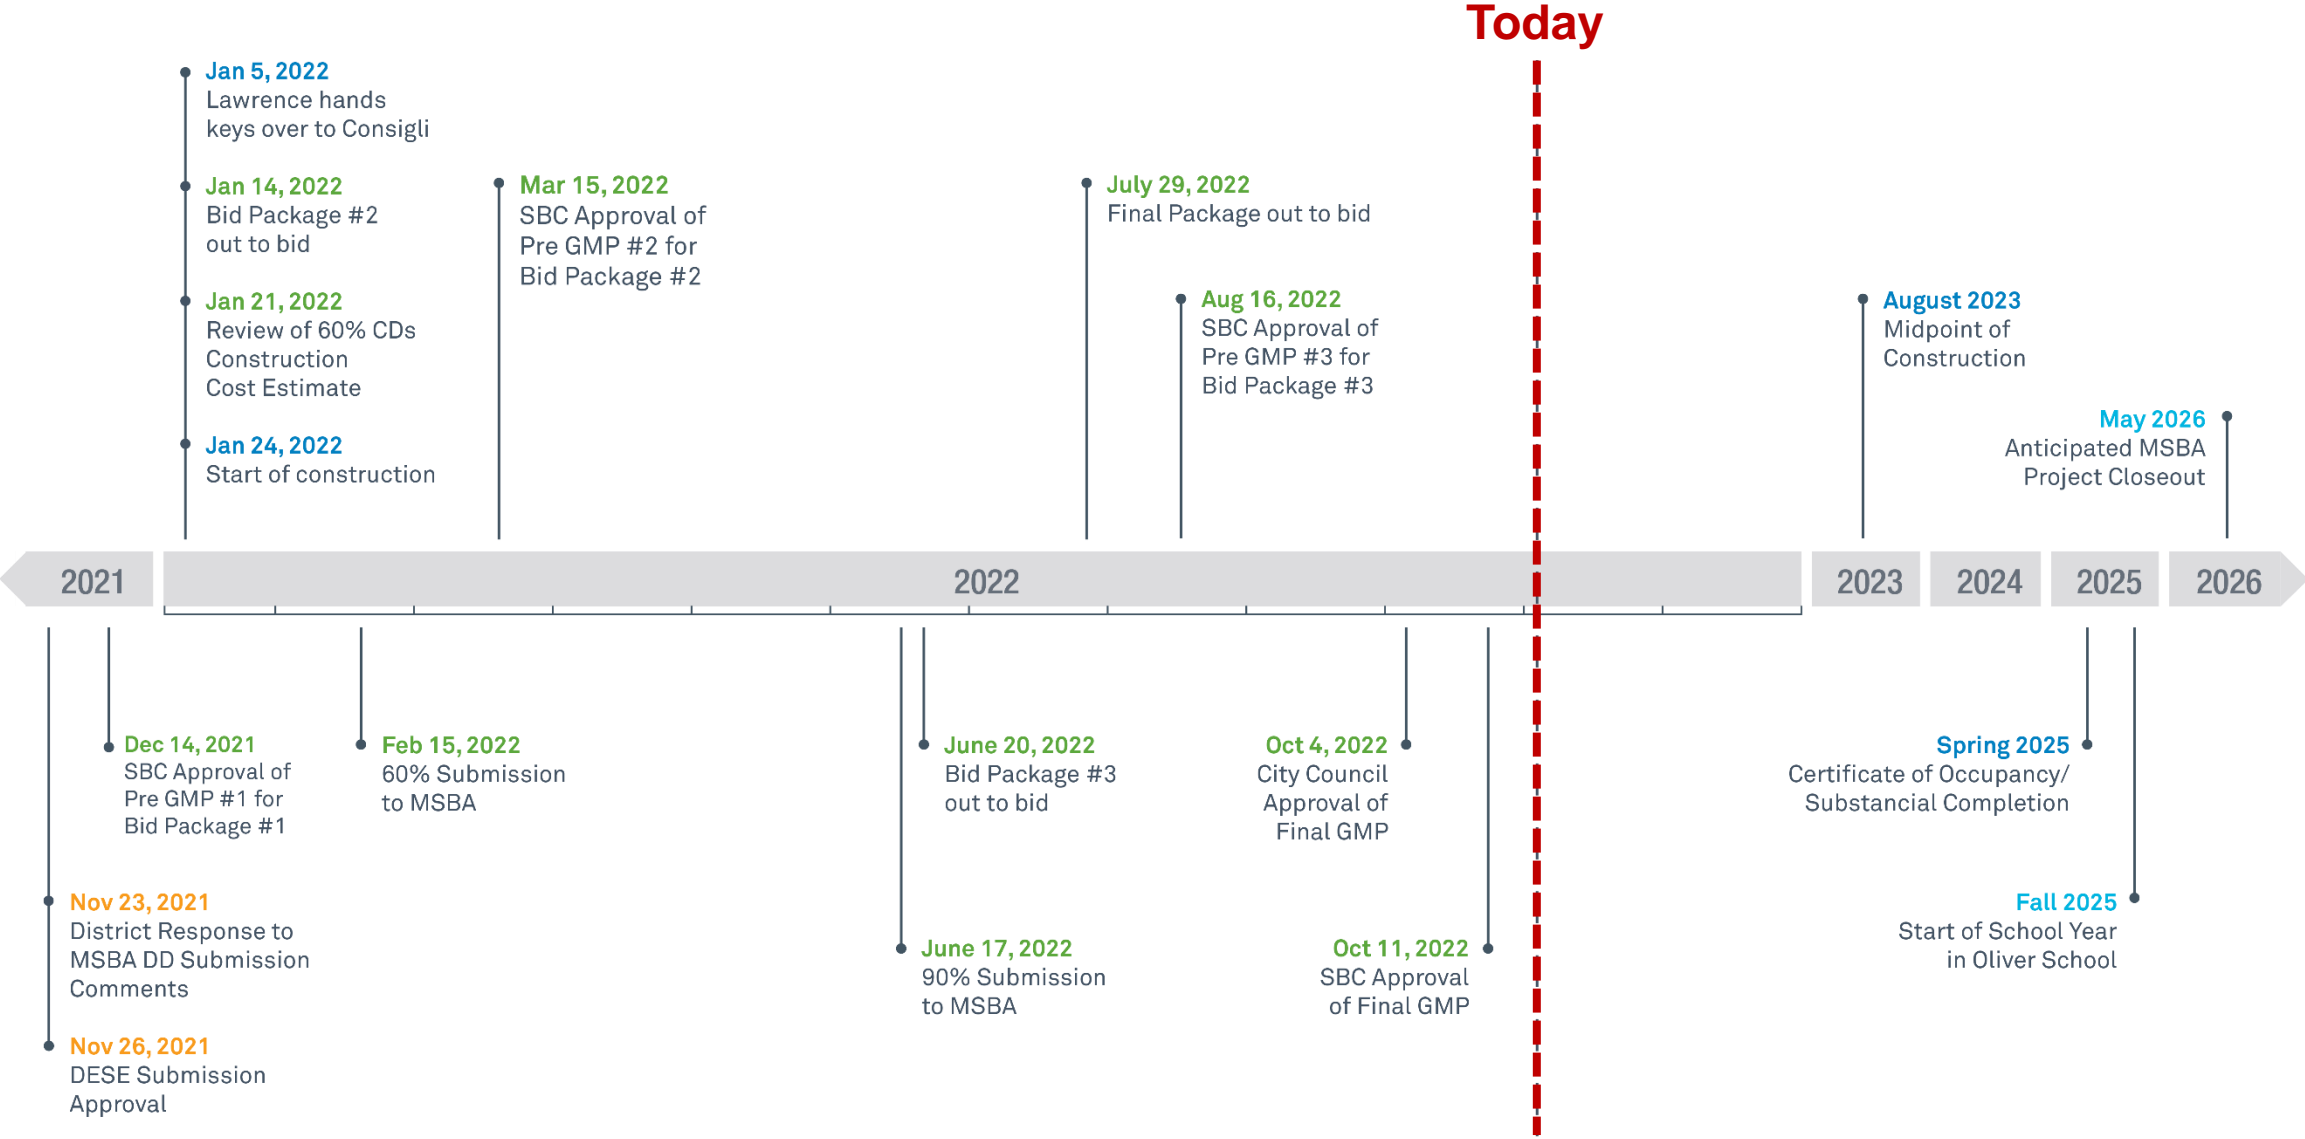

Project Status

- 10/4:
City Council Voted to Approve
Project GMP
 - 10/11:
OSSBC Voted to Approve
Project GMP
 - Utility Relocations 90%
Site Preparations 100%
Abatement & Demolition 100%
SOE Walls & Foundations: 10%
- August 2023:
Steel Erection Begins



Lawrence Oliver Monthly Update – October 2022

Link to Monthly Drone Video Footage:

<https://vimeo.com/766599124/2e6bb1a0a1>

Construction Updates

Upcoming Activities

- Install excavation bracing
- Repoint granite joints
- Excavation down to elevation 55'
- Continued disposal and transport of excavated material

Community Impacts

- Increase in truck traffic in and around construction site



Dewatering System - Jetting Process



Final Wash of Masonry Façade



Welding for Excavation Support Initiated

Drone Link:

<https://vimeo.com/766599124/2e6bb1a0a1>



Thank you!



ANSER
ADVISORY

SMMA



CONSIGLI
Est. 1905
